
BandLink 490A task map

Every hub card from `docs/tasks.md`, left to right by due date. Arrows come from each card's "Depends on" note and point from a blocker to the card it blocks. The orange chain is the longest one to the Dec 11 demo, so a slip anywhere on it moves the demo.

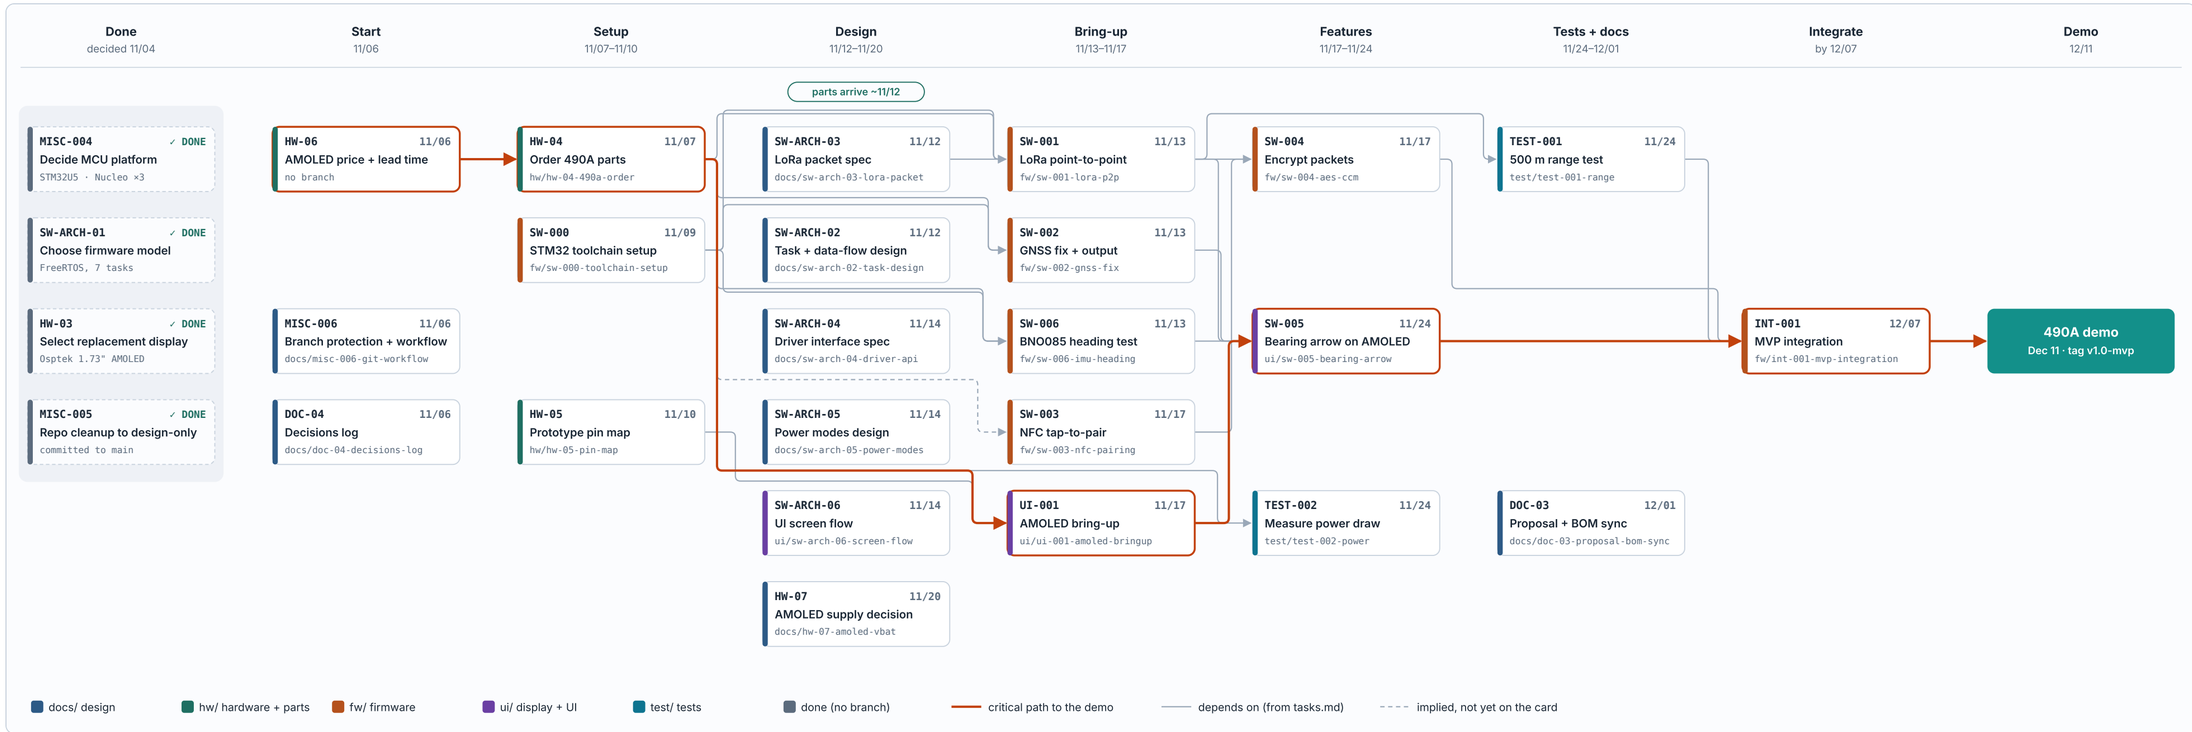

- **Critical path:** HW-06 → HW-04 → parts arrive (~11/12) → UI-001 → SW-005 → INT-001 → demo. UI-001 is on it because it's due last of the bring-up cards that SW-005 waits on. HW-06 is first, so the AMOLED quote is this week's most urgent card.
- **HW-04 fans out:** once the parts arrive, SW-001, SW-002, SW-006, UI-001 and TEST-002 (PPK2) can start.
- **INT-001** depends on SW-001 through SW-006 and TEST-001. The map draws only SW-004, SW-005 and TEST-001 into it, since those already cover the rest.
- **Gaps worth fixing in tasks.md:** SW-003 lists no blocker but needs the PN7150 from the order (dashed). The design cards (SW-ARCH-02, -04, -05, -06, HW-07) and DOC-03 also list no blockers, so nothing waits on them yet. Add a “Depends on” line wherever the team wants a design merged before the build starts.
- Owners are assigned at the team meeting.
