
BandLink projected timeline

Aug 2026 to May 2027, updated after Design Review 2 with the STM32U5 + Nucleo platform, the Osptek AMOLED, and FreeRTOS. 490A is prototype-only and ends with the Dec 11 demo; the custom PCB is built in 490B. Card IDs match the hub and docs/tasks.md.

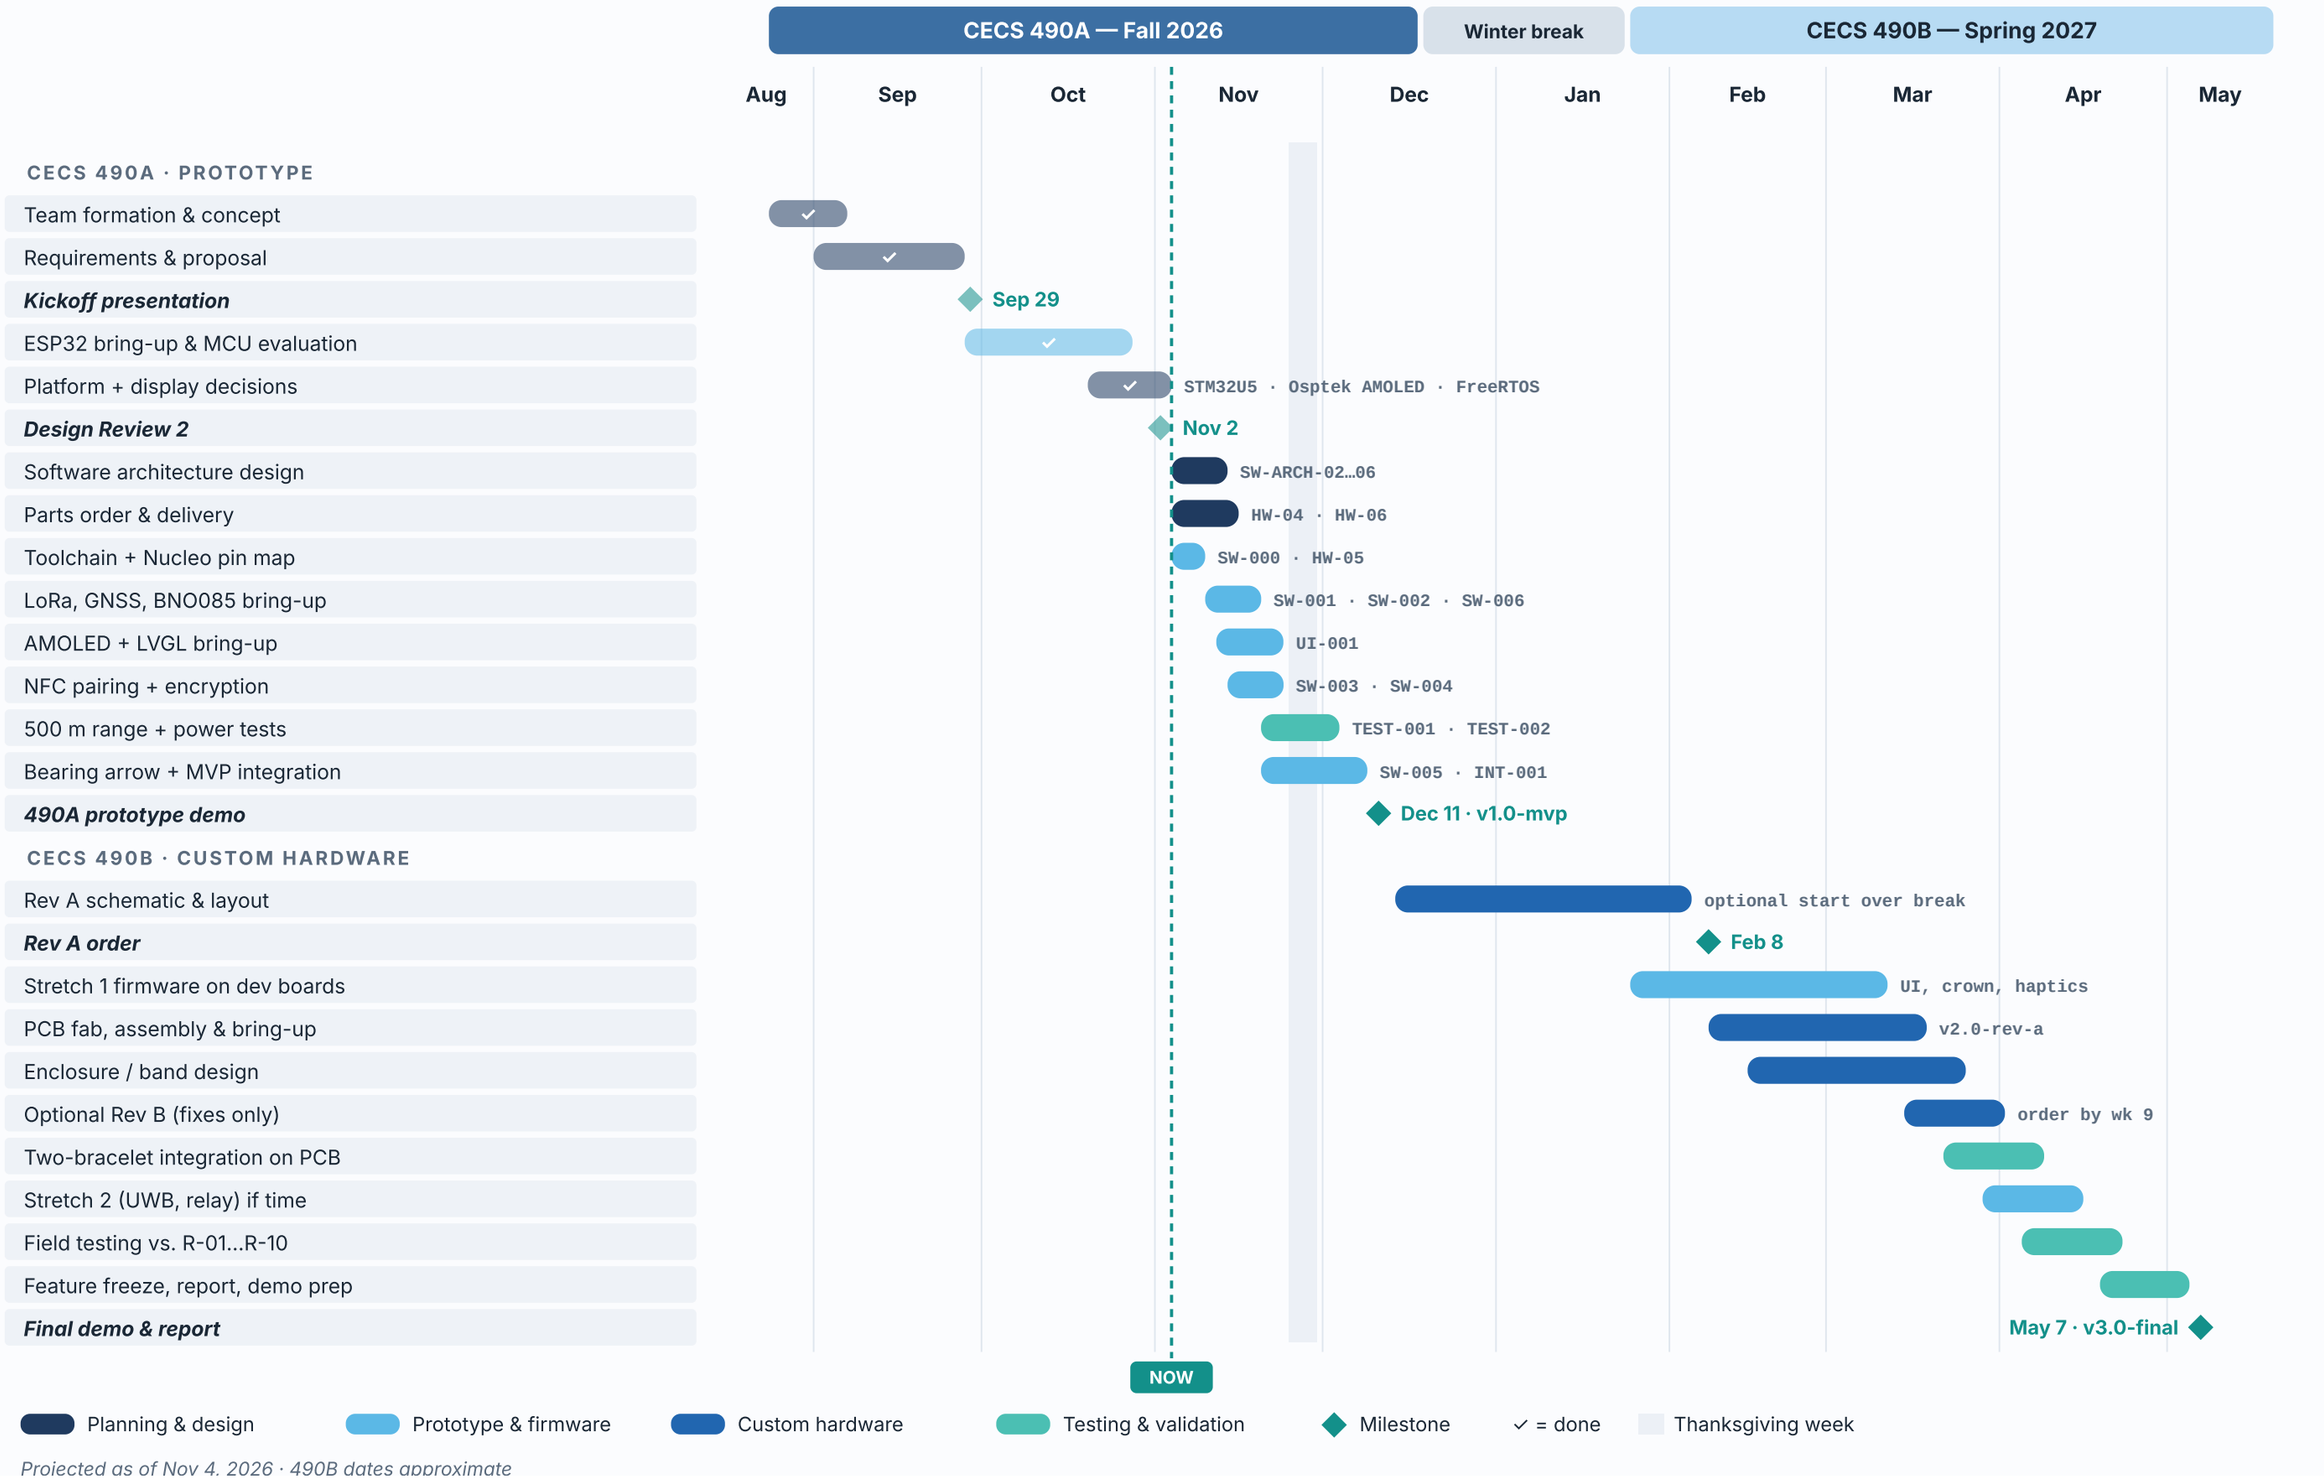

Projected as of Nov 4, 2026 · 490B dates approximate

Milestones

DATE	MILESTONE	DONE WHEN	TAG
Sep 29	Kickoff presentation	Done	
Nov 2	Design Review 2	Done	
Nov 16	Parts in hand, design docs merged	490A parts delivered; SW-ARCH-02…06 merged	
Dec 11	490A prototype demo	Two portable Nucleo units pair by NFC, exchange encrypted positions at ≥500 m, show each other's arrow and distance on the AMOLED	`v1.0-mvp`
~Feb 8	Rev A PCB ordered	Schematic and layout reviewed by the team, ERC/DRC clean	
~Mar 19	Rev A running	Custom PCB runs the MVP firmware	`v2.0-rev-a`
~Apr 2	Rev B order deadline	Only if Rev A needs fixes	
May 7	Final demo & report	R-01…R-10 verified and logged; wearable prototype; report and demo	`v3.0-final`
